

March 12, 2026

Patrick Doherty, Compliance Program Manager  
Performance Assessment Division  
Office of Energy Infrastructure Safety  
California Natural Resources Agency  
715 P Street 20<sup>th</sup> Floor  
Sacramento, CA 95814

**BY ENERGY SAFETY E-FILING**

**SUBJECT:** Southern California Edison Company's Response to Notice of Non-Performance (NON\_PAD\_SCE\_SIS\_20260114\_1300)

Dear Mr. Doherty:

Southern California Edison Company (SCE) appreciates the opportunity to provide this response to the finding identified in the Notice of Non-Performance – **NON\_PAD\_SCE\_SIS\_20260114\_1300** which SCE received on **February 12, 2026** (Notice), based on the Office of Energy Infrastructure Safety's (Energy Safety) field inspections conducted in SCE's service area on **January 14, 2026**. SCE appreciates Energy Safety's efforts to identify, communicate and work together to resolve potential wildfire risks. The enclosed response describes corrective actions taken or planned by SCE to remedy the finding identified in the Notice and to prevent recurrence.

If you have any questions, or require additional information, please contact Liz Leano at 626-302-3662 or [Elizabeth.Leano@sce.com](mailto:Elizabeth.Leano@sce.com).

Sincerely,

//s//

Brandon Tolentino  
Vice President of Wildfire and Business Resiliency  
Southern California Edison

## SCE Response

### Finding:

Notice	#	Structures
NON_PAD_SCE_SIS_20260114_1300	1	1392823E

### Summary of Findings:

Energy Safety’s Notice states that in implementing its 2025 WMP initiative 8.1.3.1 - Distribution High Fire Risk-Informed (HFRI) Inspections and Remediations (IN-1.1), SCE failed to complete clearance of down guy on Pole ID 1392823E, Grid Hardening ID 414093121-1392823E at coordinates 33.7797146678882, -118.395505159758.

Energy Safety states that it “considers this non-performance to be in the **Minor Risk category**.”<sup>1</sup>


### Response:

SCE confirms that the installation of a new guy anchor on structure 1392823E was completed on August 5, 2025. Please find photo evidence below of the guy anchor installation from August 5, 2025. SCE acknowledges that the relevant guy wire should have clearance from the rain gutter and plans to coordinate with the homeowner to

---

<sup>1</sup> Notice, p. 1.

obtain property access and complete such clearance.

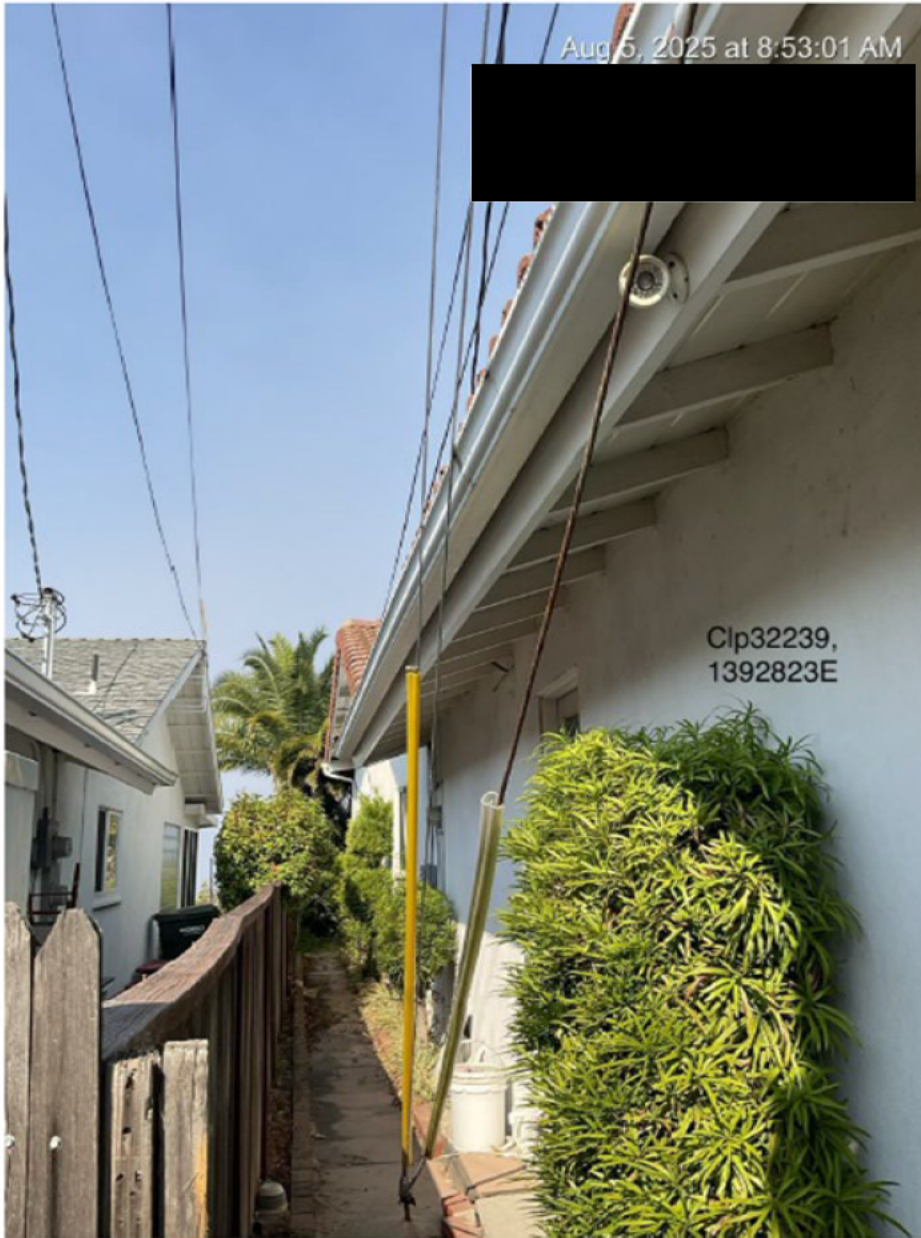

Clp32239,  
1392823E

CLP32239,1392823E

**AFTER - STA 8-STR 1392823E**

Page 6
