



2024 Liberty Work Complete QC



QC of work complete

4/10/2024, 3:38:27 PM UTC

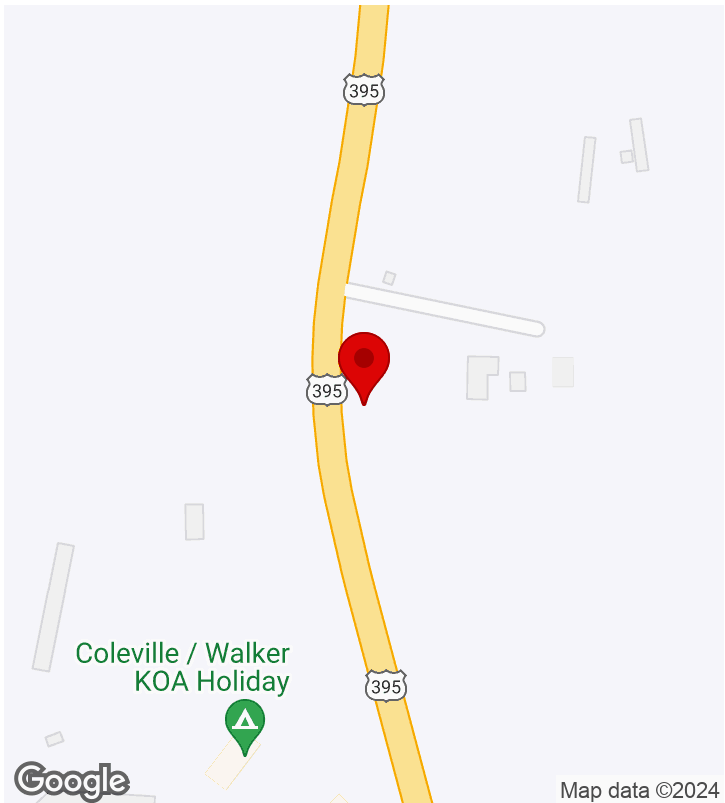

CREATED

🕒 4/4/2024, 8:52:15 PM UTC
👤 by Paul Kumro

UPDATED

🕒 4/10/2024, 3:38:27 PM UTC
👤 by Eric Oiler

STATUS

Corrective Action Completed

LOCATION

📍 38.553240, -119.502385



QC Assessment Date | April 4, 2024

Tree Information

Tree_ID	
Work_Status	
Work_Order_Circuit	
Refusal	
Date_Created	
Modified_Date	
Section	
Time Entry Date Created	
Work_Order_Span_ID	
Physical_Address	
Pole_Number	
Quantity	
Time_Entry_Quantity	
Species	
Height	
DBH	
Defect_Type	
Location_Comments	
Q1 Work Not Performed	0
Work_Type	
Q2 MCD Not Achieved or Not as Prescribed	0
Q3 Will Not Hold	3
Q4 Potential Hazard Remain	0
Cleanup_Method	
Work_Order_Comments	
Q5 Site Clean	0
Q6 ANSI Not Achieved	1
Q7 Other Trees Affected by Removal	0
Q8 Site Condition Not Stable	0
Comments	<p>Location of tag is at intersection of main line and tap. Both spans were worked, but tap still has elm and cottonwood growth at 7-8 ft below conductors. Main line span still has unworked cottonwood with growth at 8.7 ft offset below conductors. Stub and tear cuts on worked cottonwoods.</p> <p>4/9/24 4/9/24 Additional clearance achieved by tree crews, growth is now 12 below conductors. Additional photo added to show MCD achieved.</p>



Photos



