State of California – A Natural Resources Agency
OFFICE OF ENERGY INFRASTRUCTURE SAFETY
715 P Street, 15th Floor | Sacramento, CA 95814
916.902.6000 | www.energysafety.ca.gov

Gavin Newsom, Governor
Forest Kaser, Director

October 30, 2026

Brandon Tolentino
Vice President, Wildfire and Business Resiliency
Southern California Edison Company
2244 Walnut Grove Ave
Rosemead, CA 91770

NOTICE OF DATA INACCURACY

Mr. Tolentino:

Pursuant to Government Code section 15472, et seq, the Office of Energy Infrastructure Safety (Energy Safety) has conducted an inspection of work completed by Southern California Edison Company (SCE) in accordance with its 2026 Wildfire Mitigation Plan (WMP) and determined the existence of a data inaccuracy. Energy Safety therefore issues SCE a Notice of Data Inaccuracy (NODI). Failure to remedy this data inaccuracy may lead to a Notice of Non-Performance (NON) if the inaccuracy causes SCE to miss a WMP target or prevents Energy Safety from ensuring that SCE performed the targets and statements made in SCE's 2026 WMP.

On October 7, 2026, Energy Safety conducted an inspection of Southern California Edison Company's WMP initiatives in the vicinity of the city of Yucaipa, California. The inspection report is enclosed herewith. Energy Safety found the following data inaccuracies:

Data Inaccuracy 1. On Structure ID 4680049E, Grid Hardening ID TD2357977-4680049E at coordinates 34.0303981668504, -117.027191402102, the inspector observed that no covered conductor was installed at the specified location.

The data inaccuracy identified in this notice could make it appear as though SCE reached the target set in its WMP initiative WCCP Covered Conductor when it has not. If SCE does not address this data inaccuracy and includes the inaccurate data in its reporting regarding its WMP initiative WCCP Covered Conductor, Energy Safety may find that SCE failed to achieve the target for that WMP initiative. This failure may be raised in a future NON or in Energy Safety's 2026 Annual Performance Report on SCE's WMP performance.

Within 30 days from the issuance date of this NODI, SCE should provide a response advising Energy Safety of corrective actions taken or planned to remedy the identified data inaccuracy or inaccuracies.

This response shall be filed in the Energy Safety e-Filing system under the 2026 NODI Docket,[1] and the associated file name(s) must begin with the NODI identification number.

Sincerely,

/s/ Patrick Doherty

Patrick Doherty
Program Manager | Performance Assessment Division
Office of Energy Infrastructure Safety
Patrick.Doherty@energysafety.ca.gov

Cc:
Peter Van Mieghem
Peter.Vanmieghem@sce.com
Elizabeth Leano, SCE
Elizabeth.Leano@sce.com
Raghu Rayalu, SCE
Raghu.Rayalu@sce.com
Erick G Sanchez, SCE
Erick.G.Sanchez@sce.com
Sally Jeun, SCE
Sally.Jeun@sce.com
Edward Trinh, SCE
Edward.Trinh@sce.com
Samuel Isaiah, Energy Safety
Samuel.Isaiah@energysafety.ca.gov
Yana Loginova, Energy Safety
Yana.Loginova@energysafety.ca.gov
Shannon Greene, Energy Safety
Shannon.Greene@energysafety.ca.gov
AssetPerformance@energysafety.ca.gov

[1] https://efiling.energysafety.ca.gov/EFiling/DocketInformation.aspx?docketnumber=2026%20NODI

State of California – A Natural Resources Agency
OFFICE OF ENERGY INFRASTRUCTURE SAFETY
715 P Street, 15th Floor | Sacramento, CA 95814
916.902.6000 | www.energysafety.ca.gov

Gavin Newsom, Governor
Forest Kaser, Director

INSPECTION REPORT

Table 1: Inspection Location and Initiative Summary

Electrical Corporation:	Southern California Edison Company
Report Number:	PAD_SCE_SIS_20261007_1023
Date of Inspection:	October 7, 2026
City and/or County of Inspection:	Yucaipa, San Bernardino County
Inspector:	Samuel Isaiah
WMP Year Inspected:	2026
Quarterly Data Report (QDR) Referenced:	Quarter 2 (Q2)
Inspection Selection:	Energy Safety viewed the contents of the Q2 QDR and performed an analysis that resulted in the selection of the WMP initiatives and locations referenced in this report.
Relevant WMP Initiative(s):	8.2.1.1 – WCCP Covered Conductor
Inspection Purpose:	Assess the accuracy of Southern California Edison Company's QDR data, completeness of its work, and performance of WMP requirements.

Table 2: WMP Inspection Data Inaccuracies

Data Inaccuracy #	Structure ID	Grid Hardening ID	Lat/Long	HFTD	WMP Initiative Number	Data Inaccuracy Description
Data Inaccuracy 1	4680049E	TD2357977-4680049E	34.0303981668504, -117.027191402102	Non-HFTD	8.2.1.1 – WCCP Covered Conductor	Failure to provide accurate data on covered conductor installation

Observations

Data Inaccuracy 1

Findings:

On Structure ID 4680049E, Grid Hardening ID TD2357977-4680049E at 12282 Fremont St, Yucaipa, CA, 92399, USA, coordinates 34.0303981668504, -117.027191402102, the inspector observed that SCE failed to provide accurate data on covered conductor installation initiative. The inspector's observation is documented in Data Inaccuracy 1 photographs, which are attached to this report as Exhibit A.

Energy Safety concludes that there is inaccurate data because of these facts:

1. SCE reported in the 2026 Q2 QDR that work on WMP initiative 8.2.1.1 – WCCP Covered Conductor was completed at this location.
2. In 2024, SCE informed Energy Safety that stub pole work does not count toward Covered Conductor WMP totals and would either identify or exclude these points in future QDRs. This data point did not contain an identifier and was not excluded.
3. No covered conductor was observed.

This observation indicates that the data regarding covered conductor was not accurate. Failure to rectify this data inaccuracy prior to the submission of any performance assessments, such as annual reports, may result in a notice of non-performance.

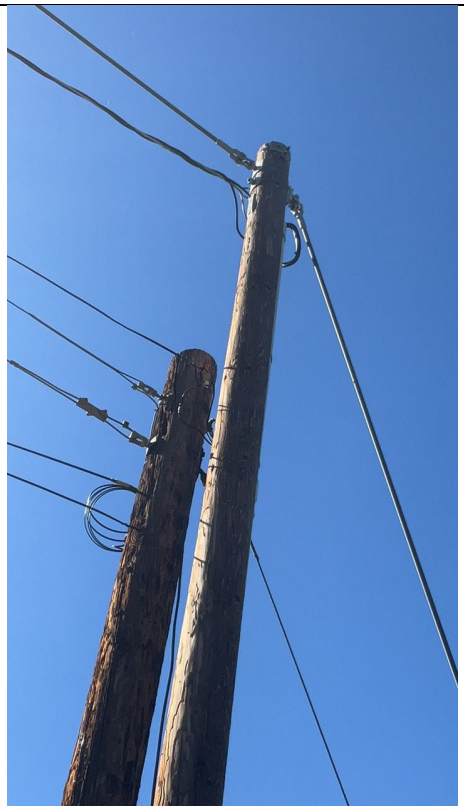
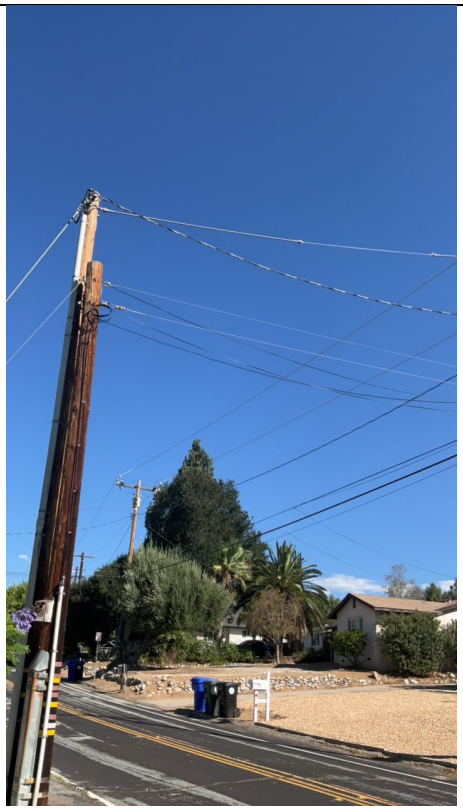
Exhibits

Exhibit A: Photo Log

Structure ID: 4680049E

Data Inaccuracy 1

	
General Image 1: Overall Structure	**General Image 2**: Structure ID

	
Asset Image 1: No covered conductor observed	**Asset Image 2**: No covered conductor observed
